# SunZia Wind Landowner Update

OCTOBER 2023

Thank you to everyone who joined us at the Community BBQ on August 17! We are so grateful to have had the opportunity to meet with you all and share a delicious meal. For those who were not able to attend, we are sorry we missed you and hope to see you at the next event. If you have questions, please don't hesitate to reach out.

# General Updates

We noted during the Community BBQ that we have been in the process of outreach for those hosting infrastructure and will wrap up this process in the coming weeks. In addition, we will provide advance notice prior to accessing your property with equipment. Last, many of you have asked, so we wanted to be sure to let you know an individualized estimated economic analysis will be forthcoming for all landowners hosting infrastructure on their property. Please keep in mind these estimates are subject to change based on final design. The letter will provide contact information for our Land Admin Team should you have any questions once received.

Finally, we would like to congratulate all the kids who participated in the county and state fairs. We enjoy seeing their hard work shine each year and watching them grow in their agricultural pursuits. We love supporting our NM youth at these events and have had the privilege of supporting dozens of kids this year.

# the privilege of supporting dozens of kids this years.

# SunZia Wind


As we progress into full construction, we are committed to providing you with regular updates on overall progress. We will approach construction on a project zone-by-zone basis. On the back is a map, construction update, and a schedule by zone of when we expect activities to occur in the northern and southern portions of the project.

### SunZia Wind South

- Clearing, road, and laydown yard construction will be ongoing in areas north of NM 247 and Corona.
   This will include county road upgrades and new road construction on private and state land.
- Quarry activities are in progress to manufacture aggregate materials.
- Construction will continue to ramp up for substation and switch yards in the Torrance Road area.
- Foundation excavation and concrete work will ramp up in late 2023 in the area north of Corona.
- General site activity and number of personnel on-site will continue to increase through early 2024.

Schedule by Zone		
Zone	Start of Construction	
1	September 2023	
2	September 2023	
3	April 2024	
4	April 2024	
5	August 2024	
6	August 2024	
7	January 2025	



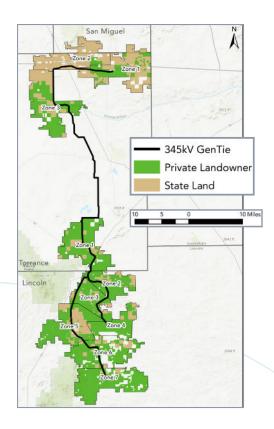

### SunZia Wind North

- Clearing and grubbing will start in January 2024.
- Quarry activities will start in January 2024 in Zone 3.
- All other activities will start in May 2024 in Zone 3 and ramp up through December 2024.
- Foundation excavation will commence in June 2024 in Zone 3.

Schedule by Zone	
Zone	Start of Construction

Zone	Start of Construction
1	December 2024
2	August 2024
3	May 2024

As a reminder, please contact us prior to entering into any third-party contracts, so we can ensure it does not conflict with your agreement.

# SunZia Transmission

We have officially begun work on the transmission line and are actively building roads and laydown yards and receiving structures and wire for the project.

As you may have seen, on September 1 Secretary of the Interior Deb Haaland joined senior elected and government officials to initiate the project's groundbreaking at the SunZia East Converter Station. This event capped over 15 years of permitting work and has allowed for construction activities to commence. Work on the transmission line is broken down into three segments with activities beginning in each zone by separate crews.



Map of the full SunZia Transmission, by segment. More detailed maps can be found at SunZia.com under "Resources."

### **Current activities**

- Building and expansion of access roads
- Laydown yards for construction trailer areas and material
  - First delivery of conductor, guy-wire, hardware, and insulators now on-site
- Staking activities along the right-of-way
- Foundation and structure work on SunZia East and West Converter Stations

## Schedule by Segment

Segment	Start of Construction
2	October 2023
3	September 2023

# Contact Us

We look forward to providing you with additional updates as we progress throughout construction and would like to thank you for hosting us in your area.

Many of you have been working on developing wind in your area for over 15 years, and we are honored to be

the partner to bring your vision to reality. If you have any questions or concerns, please feel free to contact Kyle Trojacek, field land manager for SunZia Wind, at (817) 600-1344 or our Corona Representative Barbara Sultemeier at Barbara.Sultemeier@patternenergy.com.
