

Hello Edith,

The SunZia Wind and Transmission workforce has been hard at work.

We're happy to announce that the first wind towers for SunZia Wind have been built, and almost half of the transmission line structures are in place, thanks to the over 2,000 dedicated workers on the full SunZia project.

Please check out our new video celebrating this milestone by clicking on the image below. You can share the video with family and friends on Facebook by clicking [HERE](#).




SunZia Wind Construction Update

Torrance, Lincoln & San Miguel Counties

Construction on SunZia Wind began in September of last year and is progressing on schedule. We have achieved nearly 50% completion on construction of SunZia Wind and Transmission as a whole. As a reminder, we are constructing the project on a Zone-by-Zone basis. Construction is well underway in the North and South Zones.

Below is a map of SunZia Wind's construction zones. Additional project details can be found at SunZiaConstruction.com.

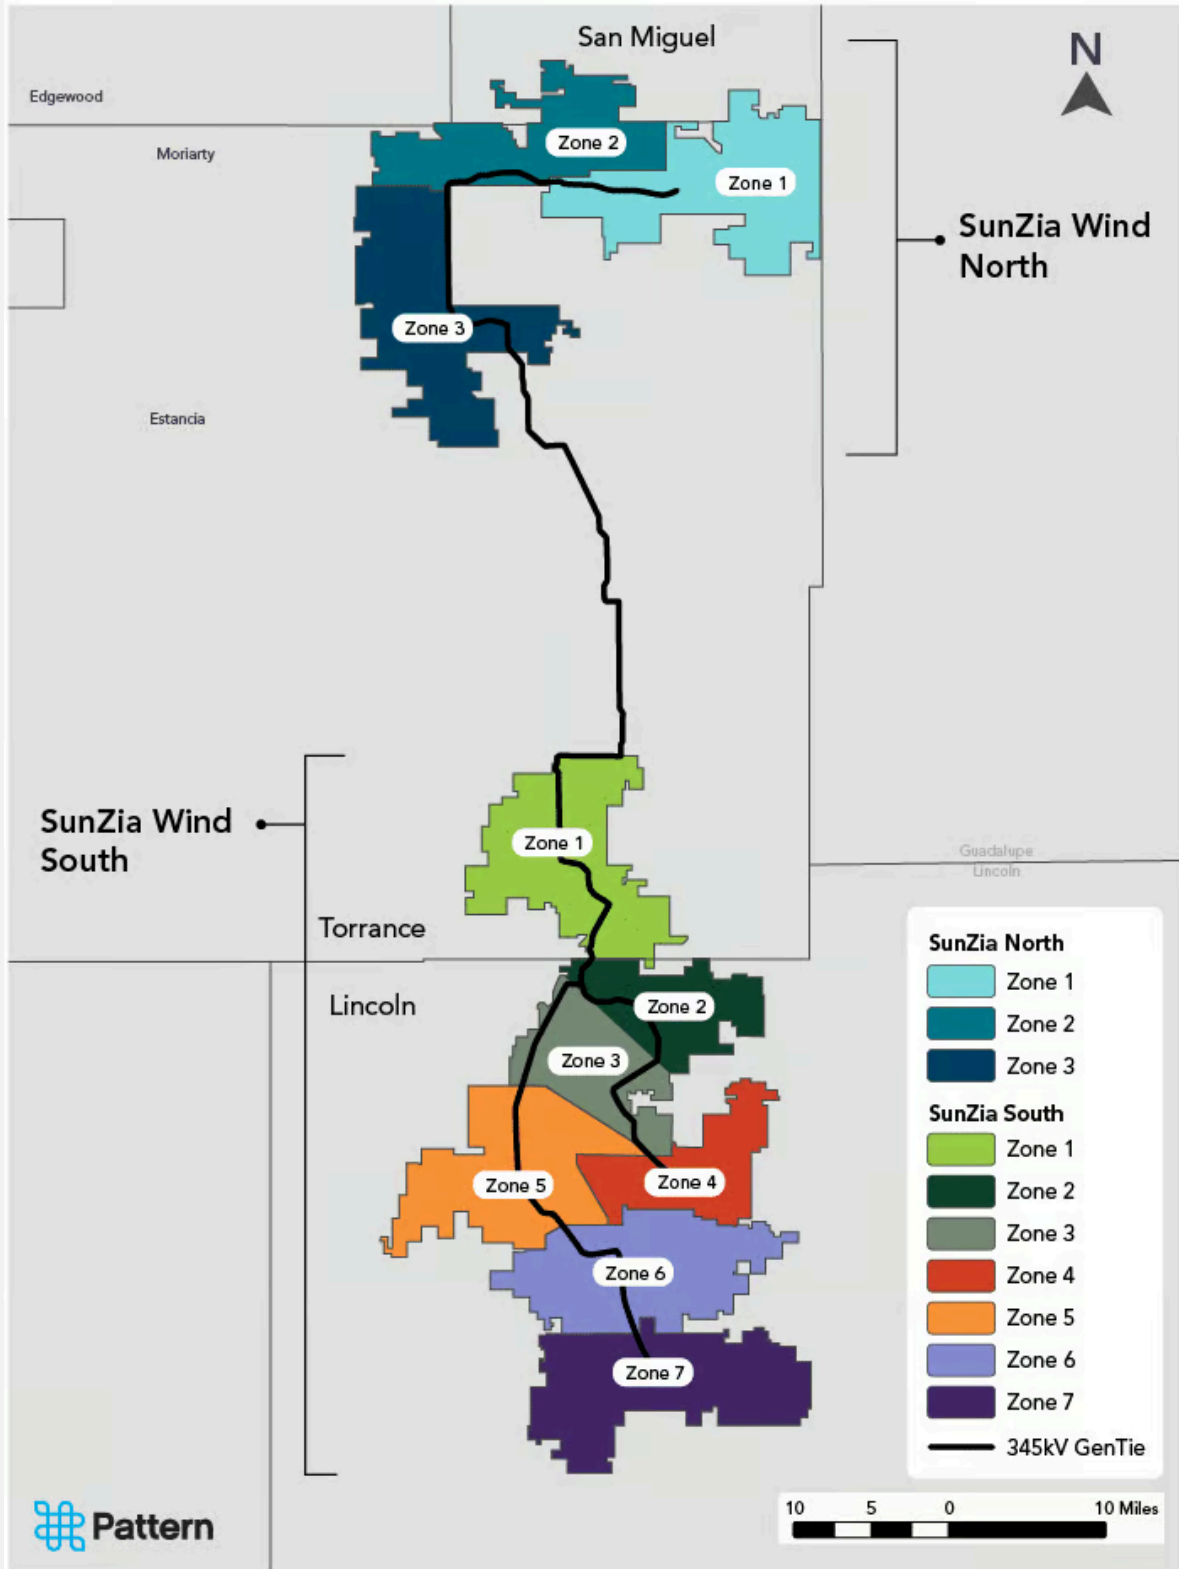

Construction crews are making progress in the North and South zones with **over 868 workers on the project.**

We continue to mobilize crews on both North and South projects. SunZia South is expected to fully mobilize by the end of this year, and SunZia North will continue until April 2025. North wind turbine generator deliveries will start in Feb 2025.

South Zone construction milestones include:

- Clearing & grubbing: 98% complete
- Access roads: 45% complete

- Wind turbines delivered: 11% complete
- Wind turbines erected: 3% complete

North Zone construction milestones include:

- Clearing & grubbing: 67% complete
- Access roads: 42% complete
- Foundations poured: 37% complete
- Foundations excavated: 49% complete



SunZia Wind South Turbine Tower Deliveries Update

Turbine tower and component deliveries began in June along Highway 42. We appreciate your patience with the delivery traffic, but the good news is that we are scheduled to complete the majority of turbine deliveries using the current route by the end of November 2024.

Deliveries on Highway 42 will decrease in frequency going forward, but there will be deliveries along the current route until the end of November 2024. Recently, the turbine deliveries location has shifted, with delivery trucks coming all the way into Corona and turning onto Highways 54 and 247. When deliveries start on Highway 247 in late October 2024, there will be one way traffic restrictions on Highway 247, similar to what is in place on Highway 42.

As with our partial closure of Highway 42 over the last few months, our team has been working with local school districts to ensure that this new delivery traffic on Highways 54 and 247 does not impact bus schedules and school transportation.

We will continue to keep you updated on traffic changes as construction progresses, and we appreciate your patience throughout the delivery of the wind turbine towers and components.

Contact Us

We will continue to provide updates as construction progresses on SunZia Wind and Transmission. Thank you for your continued partnership and hosting us in your community. As a landowner, you are assigned a land agent. If you have construction activity related questions, please reach out to your land agent. If you are unsure who that is, please contact Tyler Shepherd at Tyler.Shepherd@patternenergy.com or 806-346-9851.

For all other SunZia inquiries, please email SunZia@patternenergy.com or call (855) 780-3859.

Sincerely,
SunZia Wind

Sent to: edith.camargo-renteria@patternenergy.com

[Unsubscribe](#)

Pattern Energy, 317 Commercial Street NE, Suite 100, Albuquerque, New Mexico 87102, United States
